

**COMPANY CONFIDENTIAL
WATERS CORPORATION
2695 System Prep Check Off Sheet**

Part Number: 186269506	Date: 16/Nov/2018
Serial Number L18SM4610A	Control # NA

Description	Serial Number	Revision	Comments
Front Panel PCB	301018150M	C	210000384
Fluidics Driver PCB	171018600M	K	210000416
CPU (Check for current revision.)	021118233M	F	210000411
Power Supply	EK00642	N/A	WAT 270471-01
Heater/Cooler PCB (if applicable)	101018018M	C	210000444
Customer Information Set	N/A	NA	NA

	Test	Prep
1. System purge complete.	☒	☒
2. Check carousels are removed from unit.	☒	☒
3. Green I/O B and A connectors are on the back of the CPU.	☒	☒
4. Verify the following labels are on the unit	☒	☒
• Instrument serial labels on front and back of unit & Heater/Cooler serial #'s (if applicable)		
• Exclamation point on the front panel above the solvent door.		
• ETL Label		
• Power supply labels (On the rear & top of the power supply)		
• Verify correct Waters logo label is used for product built.		
5. Check cables are secure to PCB's. (Especially the large gray cable).	☒	☒
6. Verify the pump torpedo assemblies are secured to the tray.	☒	☒
7. Verify the pump tray and solvent tray captive screws are secure.	☒	☒
8. Verify the pump and solvent doors do not rub when closed.	☒	☒
9. Verify all hardware on each sub assembly is fully tightened.	☒	☒
10. Check the draw off valve is closed on the pump tray.	☒	☒
11. Visually inspect unit for paint defects and fix accordingly.		☒
12. Verify all notes are removed from the instrument.	☒	☒
13. Verify that the following paperwork is in the folder and complete.	☒	☒
• Final Test Record		
• Pump check off sheet		
• System Prep Check Off Sheet		
14. Certificate of Functional Performance is visible through the window.		☒
Comments: DE - SKW - 00000046 (TMD010532)		
DE - SKW - 00000069 (TMD010508)		
DE - SKW - 00000084 (TMD010578)		
HEATER COOLER: L18SHC167A		
- END OF DATA -		
Ship preparation completed by: <u>Ang Kin Chung</u>	Date: 19 Nov 2018	

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

WATERS CORPORATION - TEST RECORD

Part Number:	186269506	Product:	eAlliance
Operator:	lgba / Jernail	Start Date/Time:	16 NOV 2018 / 16 25
Serial Number:	48SM4610A	End Date/Time:	19 NOV 2018 / 08 34
Test System:	3/2	Order:	N/A
Test Software:	Empower2	Location:	5th Floor Flex

TMD: N/A

Firmware: 3.04

Test Name	LSL	Measurement	USL	Unit	Outcome		
Electrical Safety Tests	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
System Initialization	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Power Supply Fan Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Unit Fan Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Keypad Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Display Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Rear Panel Tests	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Degasser Test (if equipped)	—	0.6	1.3	PSIA	PASS ☒	FAIL ☐	See Event Log ☐
Spurge Valve Test (if equipped)	—	—	—	—	PASS ☐	FAIL ☐	See Event Log ☐ N/A
Heater/Cooler Test (if equipped)	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Solvent Inlet Plumbing Verification	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Sealwash Test (if equipped)	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Needle Wash Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
System Leak Test	—	48.60	160	PSI	PASS ☒	FAIL ☐	See Event Log ☐
Injector Adjustment Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐
Top	38	48	50	Steps			
Width	60	75	90	Steps			
Compression Test	—	9.9	50	PSI	PASS ☒	FAIL ☐	See Event Log ☐
Z-Ram Height Test	—	—	—	—	PASS ☒	FAIL ☐	See Event Log ☐

WATERS CORPORATION - TEST RECORD

Part Number: 186269506

Serial Number: U8SM4610A

Test Name	LSL	Measurement	USL	Unit	Outcome		
Carrier-Alignment/RV Injection Test	---	---	---	---	PASS ☒	FAIL ☐	See Event Log ☐
Carryover Test	---	0	0.002	%	PASS ☒	FAIL ☐	See Event Log ☐
Linearity – X-Intercept	---	0.458	1.0	---	PASS ☒	FAIL ☐	See Event Log ☐
Linearity – R-Squared	0.999	1.0000	---	---	PASS ☒	FAIL ☐	See Event Log ☐
AC Precision Test	---	---	---	---	PASS ☒	FAIL ☐	See Event Log ☐
RT Precision	---	0.0012	0.0090	Min.			
Area Precision	---	0.086	0.5	% RSD			
PSI Ripple	---	13.76	65	PSI			
BD Precision Test	---	---	---	---	PASS ☒	FAIL ☐	See Event Log ☐
RT Precision	---	0.0008	0.0090	Min.			
Area Precision	---	0.049	0.5	% RSD			

Note: Fill in 'N/A' if not applicable.

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Instrument Final Test Overall Result -

PASS ☒

FAIL ☐



Signed: gbar 1064627

Date: 19 NOV 2018

END OF DATA

Part Number: 186269506
 Tested By: JERNAIL
 Serial Number: L18SM4610A
 UUT Firmware: 3.04

Description: 2695 Separations Module
 Test Template Revision: 1.8
 Test Station: Final-test-3
 System: 2695_3

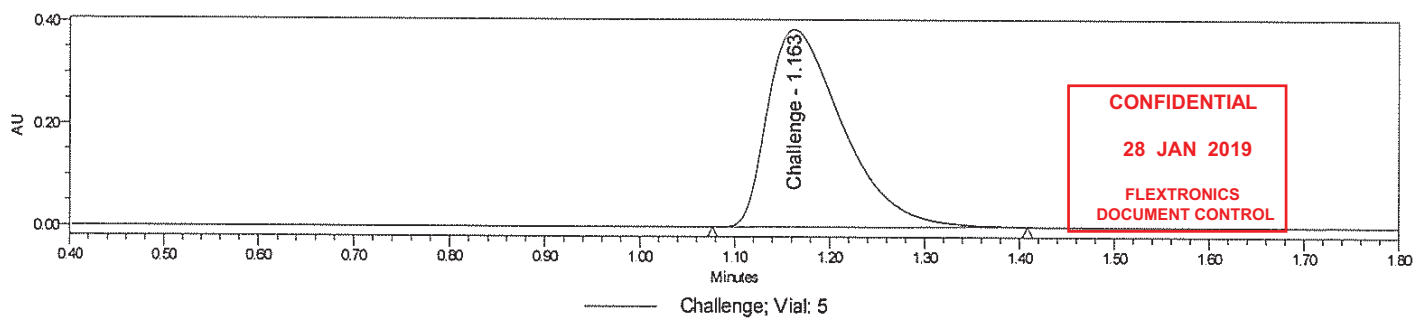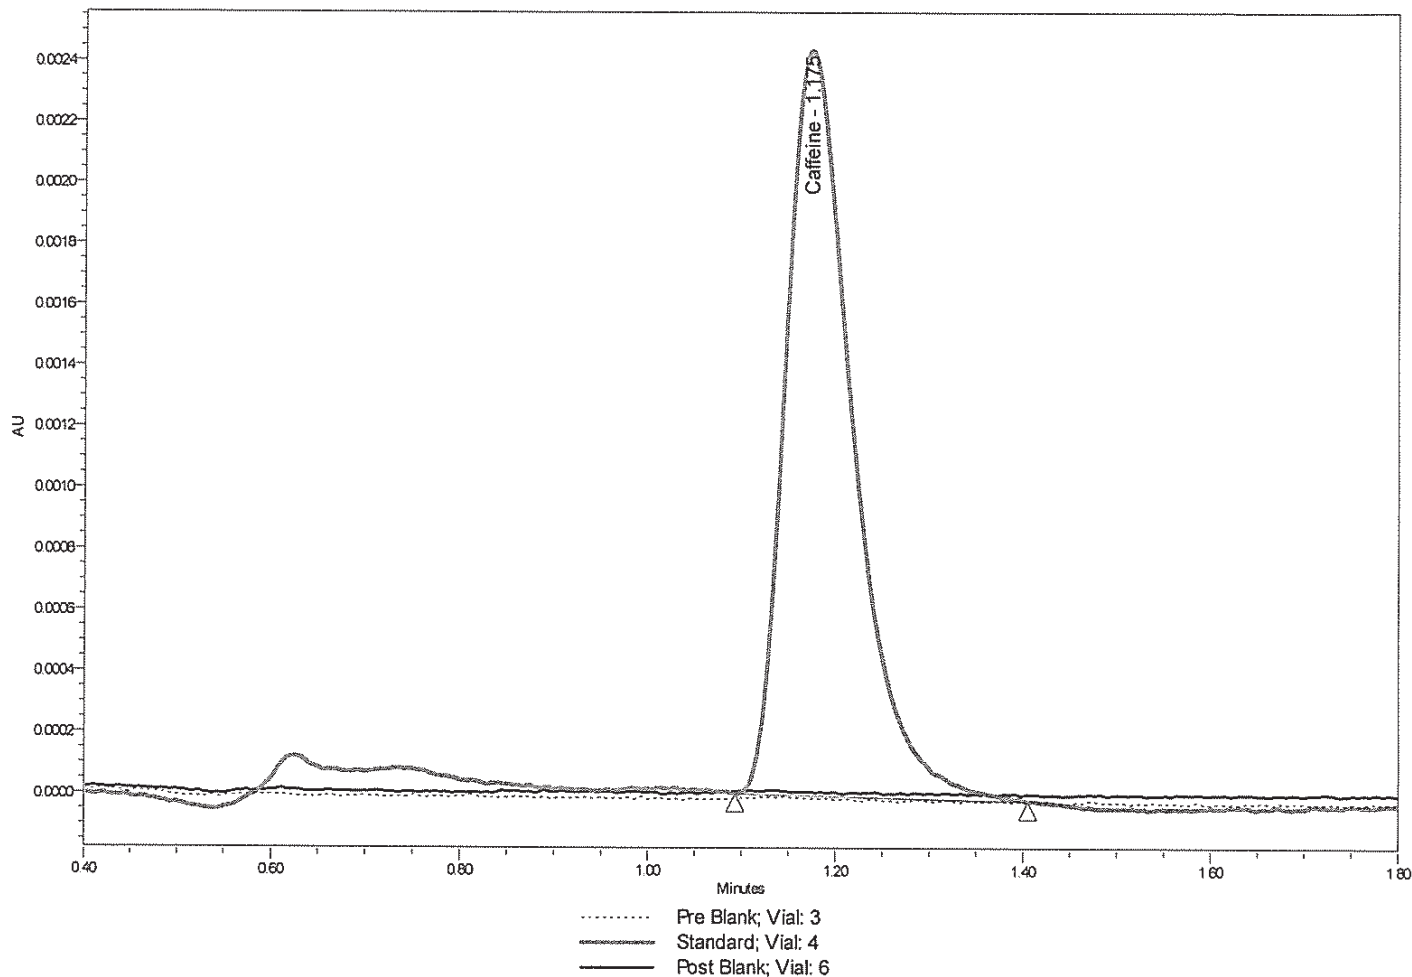

	Date Acquired	SampleName	Area	Percent
1	11/17/2018 3:05:40 PM SGT	Pre Blank		
2	11/17/2018 3:08:21 PM SGT	Standard	12192	0.0100
3	11/17/2018 3:11:01 PM SGT	Challenge	2117921	
4	11/17/2018 3:26:56 PM SGT	Post Blank		

Carryover Test:
 PreBlank injection (to establish system cleanliness)
 Standard (0.4 PPM) Caffeine injection
 Challenge injection (10,000 X Standard = 4,000 PPM)
 PostBlank injection
 Carryover (%) = Carryover Area/Standard Area * 0.010

Specification: Post Blank Percent < 0.002
 (or Blank peak(s) missing/blank)

This Test Record and any data contained within it are proprietary to Waters Corporation and must be retained by Waters for the time period prescribed in its Quality Records Retention Policy. If any of the individual tests fail; a note must be referenced that details the work performed to correct that specific deficiency. An overall failure indicates a special circumstance in which case a complete retest is to be done. A second form is required to document that testing; the initial form must be attached and retained.

Part Number: 186269506

Tested By: JERNAIL

Serial Number: L18SM4610A

UUT Firmware: 3.04


Description: 2695 Separations Module

Test Template Revision: 1.8


Test Station: Final-test-3

System: 2695_3

Overlaid Caffeine Peak Chromatograms

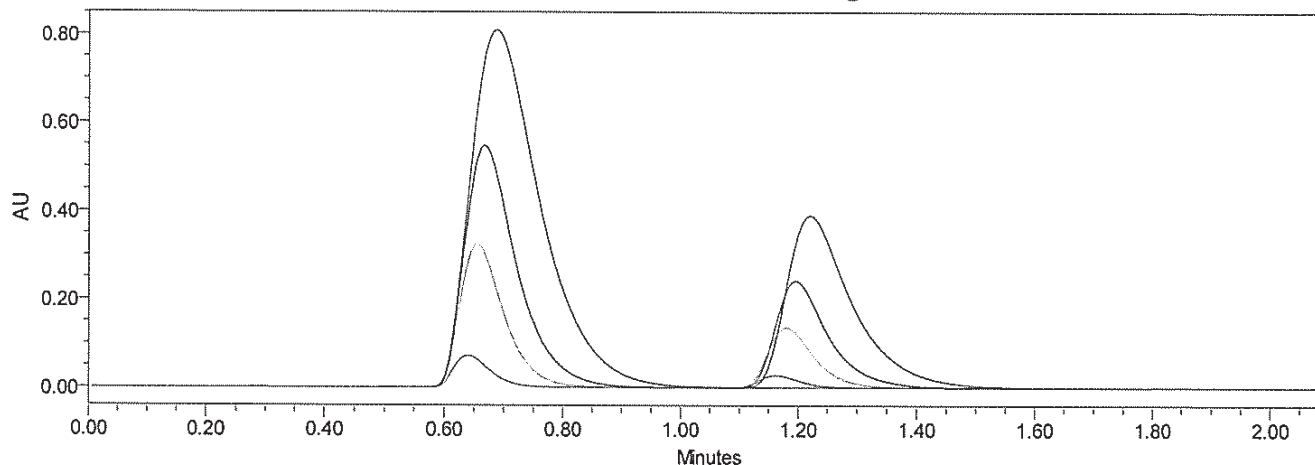

Calibration Plot

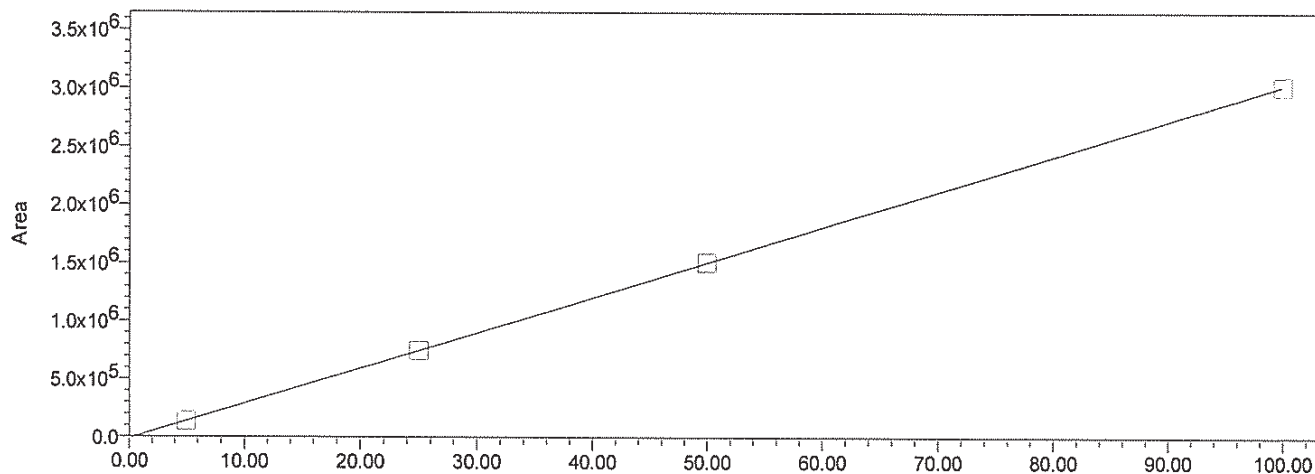

Injection Linearity and Accuracy

Fit Type Linear (1st Order)

A -13914.446867

Equation $Y = 3.04e+004 X - 1.39e+004$

B 30351.988235

X_Intercept 0.458

R^2 1.0000

$1-(A/B) = X \text{ Intercept (ul)}$
Specs: $R^2 \geq 0.999$, $|X\text{-Intercept}| \leq 1.0 \text{ ul}$

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

This Test Record and any data contained within it are proprietary to Waters Corporation and must be retained by Waters for the time period prescribed in its Quality Records Retention Policy. If any of the individual tests fail, a note must be referenced that details the work performed to correct that specific deficiency. An overall failure indicates a special circumstance in which case a complete retest is to be done. A second form is required to document that testing; the initial form must be attached and retained.

Part Number: 186269506
Tested By: JERNAIL
Serial Number: L18SM4610A
UUT Firmware: 3.04

Description: 2695 Separations Module
Test Template Revision: 1.8
Test Station: Final-test-3
System: 2695_3

Component Summary For Retention Time

	Sample	Vo	Caffeine
1	Precision AC	0.6514	1.1788
2	Precision AC	0.6524	1.1803
3	Precision AC	0.6500	1.1784
4	Precision AC	0.6525	1.1809
5	Precision AC	0.6502	1.1792
6	Precision AC	0.6522	1.1812
Std. Dev.		0.0011	0.0012

Component Summary For Area

	Sample	Caffeine
1	Precision AC	3539081
2	Precision AC	3539705
3	Precision AC	3536469
4	Precision AC	3542218
5	Precision AC	3537725
6	Precision AC	3533338
% RSD		0.086

Component Summary For Pressure_Ripple


	Date Acquired	
1	11/17/2018 3:45:51 PM SGT	16.15
2	11/17/2018 3:48:36 PM SGT	12.91
3	11/17/2018 3:51:19 PM SGT	13.44
4	11/17/2018 3:54:04 PM SGT	14.06
5	11/17/2018 3:56:47 PM SGT	11.68
6	11/17/2018 3:59:28 PM SGT	14.29
Mean		13.76

Specifications:


Retention Time Standard Deviation: ≤ 0.0090 min

Area % RSD: ≤ 0.500

Mean Pressure Ripple < 65 PSI

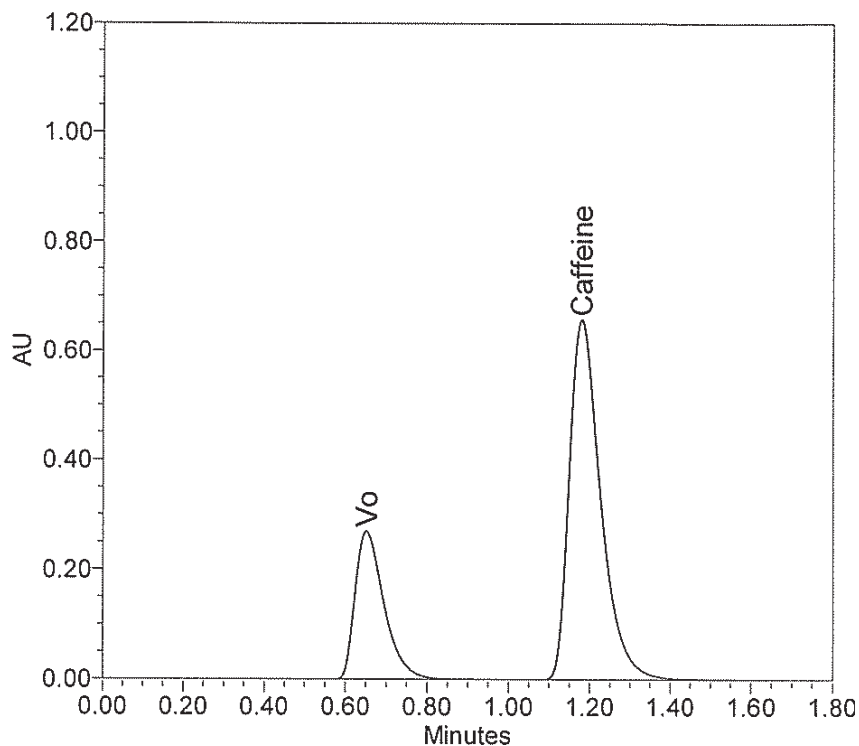

SYSTEM PRESSURE (PSI)

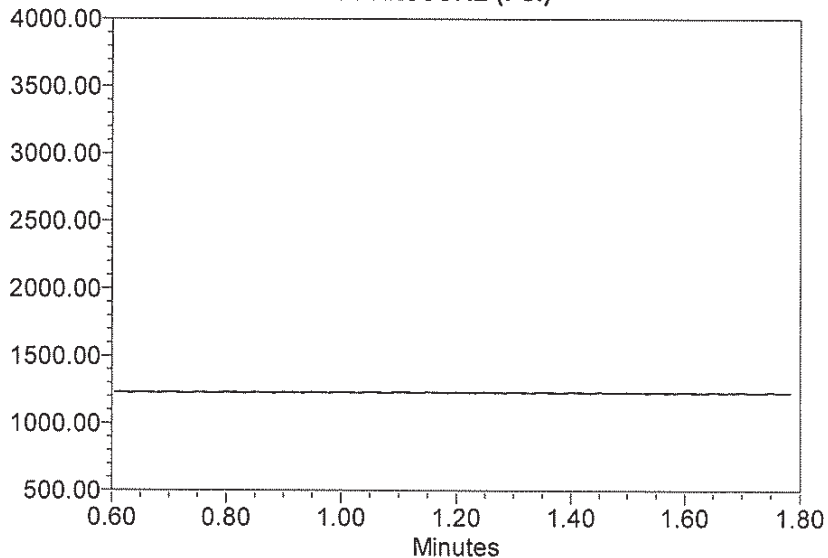

CONFIDENTIAL


28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

This Test Record and any data contained within it are proprietary to Waters Corporation and must be retained by Waters for the time period prescribed in its Quality Records Retention Policy. If any of the individual tests fail, a note must be referenced that details the work performed to correct that specific deficiency. An overall failure indicates a special circumstance in which case a complete retest is to be done. A second form is required to document that testing; the initial form must be attached and retained.

Part Number: 186269506
 Tested By: JERNAIL
 Serial Number: L18SM4610A
 UUT Firmware: 3.04

Description: 2695 Separations Module
 Test Template Revision: 1.8
 Test Station: Final-test-3
 System: 2695_3

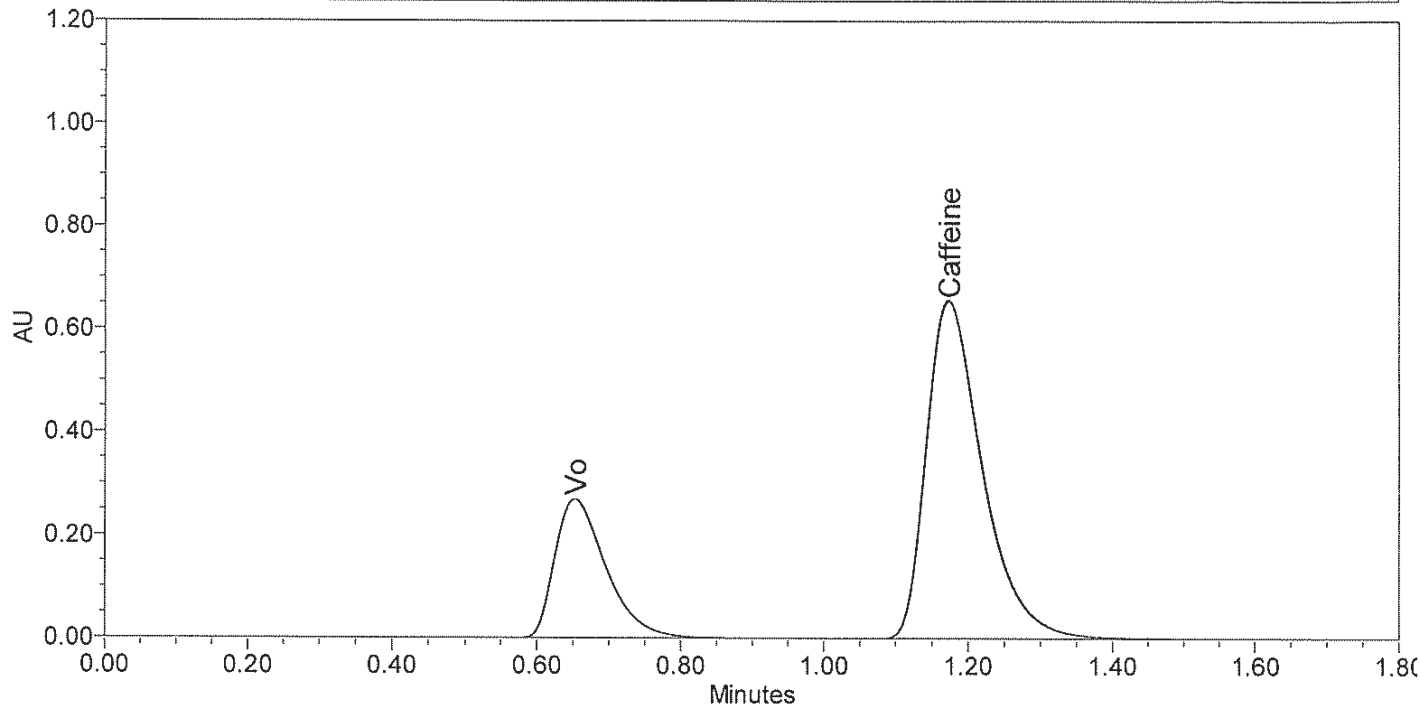

Component Summary For Retention Time

	Sample	Date	Vo	Caffeine
1	Precision BD	11/17/2018 4:13:19 PM SGT	0.6530	1.1736
2	Precision BD	11/17/2018 4:16:02 PM SGT	0.6525	1.1730
3	Precision BD	11/17/2018 4:18:47 PM SGT	0.6522	1.1727
4	Precision BD	11/17/2018 4:21:30 PM SGT	0.6533	1.1739
5	Precision BD	11/17/2018 4:24:11 PM SGT	0.6513	1.1716
6	Precision BD	11/17/2018 4:26:52 PM SGT	0.6523	1.1728
Std. Dev.			0.0007	0.0008

Component Summary For Area

	Sample	Date	Caffeine
1	Precision BD	11/17/2018 4:13:19 PM SGT	3538564.25
2	Precision BD	11/17/2018 4:16:02 PM SGT	3537579.12
3	Precision BD	11/17/2018 4:18:47 PM SGT	3535633.23
4	Precision BD	11/17/2018 4:21:30 PM SGT	3538690.38
5	Precision BD	11/17/2018 4:24:11 PM SGT	3536402.83
6	Precision BD	11/17/2018 4:26:52 PM SGT	3534339.82
% RSD			0.049

Specifications:
 Retention Time Standard Deviation: <= 0.0090 minutes
 Area % RSD: <= 0.500

This Test Record and any data contained within it are proprietary to Waters Corporation and must be retained by Waters for the time period prescribed in its Quality Records Retention Policy. If any of the individual tests fail, a note must be referenced that details the work performed to correct that specific deficiency. An overall failure indicates a special circumstance in which case a complete retest is to be done. A second form is required to document that testing; the initial form must be attached and retained.

CONFIDENTIAL

28 JAN 2019

**FLEXTRONICS
DOCUMENT CONTROL**

Waters Corporation

SUBASSEMBLY TEST RECORD

Part Number:	289000526	Description:	Alliance Pump Tray
Tested By:	246158	Date:	11/16/2018 10:46:25 AM
Serial Number:	45J0H076	Control Number:	N/A
Software Revision:	N/A	Factory Order:	N/A

Seal Wash Functional Test PASS ☒ FAIL ☐ see note # _____ PASS ☐

Accumulator Decay Test

Total decay (≤ 150 psi) - Actual: 40 PSI PASS ☒ FAIL ☐ see note # _____ PASS ☐
Compress Volume (≤ 20 %) - Actual: 19 % PASS ☒ FAIL ☐ see note # _____ PASS ☐

Primary Decay Test

Total decay (≤ 150 psi) - Actual: 2 PSI PASS ☒ FAIL ☐ see note # _____ PASS ☐
Compress Volume (≤ 20 %) - Actual: 12 % PASS ☒ FAIL ☐ see note # _____ PASS ☐

Flow Rate Test [Measured Flow: 1.001 ml/min]
($\leq \pm 1\%$) - Actual: 0.10 % ERROR PASS ☒ FAIL ☐ see note # _____ PASS ☐

Ripple Test
($\leq 2.5\%$) - Actual: 1.4 % PASS ☒ FAIL ☐ see note # _____ PASS ☐

Pump Tray Result: PASS ☒ FAIL ☐ Signed: Shao Yan 246158 Date: 16/Nov/2018

Notes: NA

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Pump PCB S/N: 220918207M Accum. Xducer S/N: 276059 Prim. Xducer S/N: 275931

This Test Record and any data contained within it are proprietary to Waters Corporation and must be retained by Waters for the time period prescribed in its Quality Records Retention Policy. If any of the individual tests noted above fail, a note must be referenced that details the work performed to correct that specific deficiency. An overall failure indicates a special circumstance in which case a complete retest is to be done. A second form is required to document that testing; the initial form must be attached and retained.



WATERS Instrument Assembly Event Log

(1) INSTRUMENT SN: <u>L18SM 4610 A</u>						
(2) S/NO	(3) Date/Time	(4) Event	(5) Event Category	(6) Actions taken for Resolution	(7) DPTF	(8) Performed by (Badge No, Sign and Date)
NA						

Event Category:-

- 1.1 Tightening of hardware and fittings
- 1.2 Reseating of connections (cables, PCB tubing, fittings etc.)
- 1.3 Alignments/Adjustments (Door, sensors, optics etc.)
- 1.4 Re-run test due to test equipment/computer issues or because the instrument was not fully equilibrated.
- 1.5 Installation of missing components
- 1.6 Correction of PCB jumper position
- 1.7 Other

Note:

- 1) For Test failures, refer to respective instrument Final test record
- 2) For Part Replacement, refer to respective instrument Traceability Record

Review:

Resolutions have been taken and unit has passed required testing.

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

(9) Badge No, Sign and Date:	246025 <u>h</u> 19 Nov 2018
---------------------------------	-----------------------------

This Document is controlled in FlexQ. All Copies (electronic or printed) are considered uncontrolled.
Users must verify the revision of such uncontrolled copy in FlexQ before its use.





SKW-ENG4028-00
Final Inspection Checklist Template

Rev: A


Final Inspection Checklist For
279003915
WAT-RW-SKI04675 Rev A

Model : 279003915	Checked By : (Employee Number & Sign) 1025464 Rspg	Date : 1 6 - N O V - 2 0 1 8
Serial No : 46J9D028	Verified By : (Employee Number & Sign) 947378 J	Date : 1 6 - N O V - 2 0 1 8


NOTE: Tick in the box means verified and accepted.

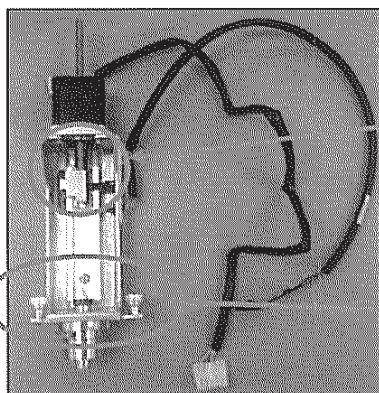


☒ a) Ensure linear slide is tight and secured properly.



☒ b) Ensure 2 captive screws are present.

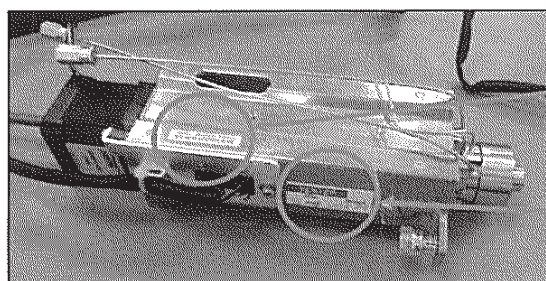

☒ c) Correct serial no label is pasted.
(As shown in example)



☒ d) Ensure TESTED label is present and signed.
(As shown in example)

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

COMPANY CONFIDENTIAL

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.

FLEXTRONICS

Document No. : WAT-RW-SKI02365	Rev: B	Final Inspection Check List	Checked By : (Badge# & Sign) 1036480 PARA	Date : 16 - NOV - 2018
Model : WAT271290	Serial No. : 46JDC044		Verified By : (Badge# & Sign) 947378 of	Date : 16 - NOV - 2018



NOTE: Tick in the box means verified and accepted.

Assy,Molded Carousel Drive



b)



c)

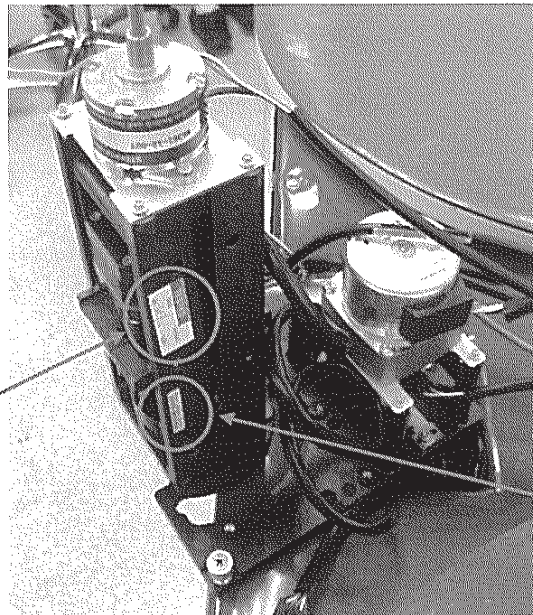

a)



d)



☒ a) Ensure all carousel screws are fully tighten.

☒ b) Ensure Ground wire is fully tighten onto Carousel Drive.

☒ c) Ensure TESTED label is present and signed (As shown in example)

☒ d) Ensure correct serial no label is pasted (As shown in example)

Remarks:

NA

CONFIDENTIAL

28 JAN 2019


FLEXTRONICS
DOCUMENT CONTROL

This Document is controlled in FlexQ. All Copies (electronic or printed) are considered uncontrolled.
Users must verify the revision of such uncontrolled copy in FlexQ before its use.

Model : 186269506	Checked By : (Employee Number & Sign) 246025 <i>[Signature]</i>	Date : 1 9 - NOV - 20 1 8
Serial No. : L18SM4610A	Verified By : (Employee Number & Sign) 836410 <i>[Signature]</i>	Date : 1 9 - NOV - 20 1 8

Front view


NOTE: Tick in the box means verified and accepted.

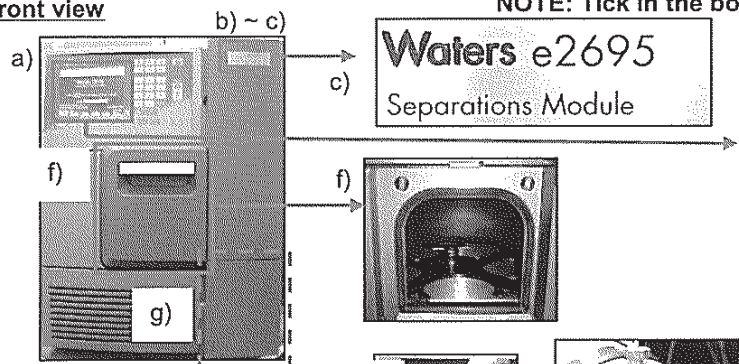


d) e.g.:





e) e.g.:



e) e.g.:



Open the doors

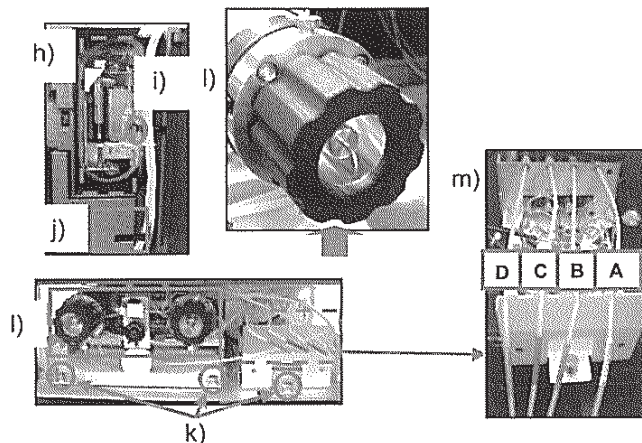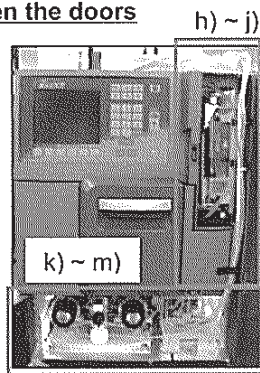

- ☒ a) Overall appearance check, no scratches, stain mark & etc. keypad surface also included.
- ☒ b) Check snap-in badge is fully catch to syringe door.
- ☒ c) Remove protective sheet for Waters logo.
- ☒ d) Check "alliance" is displayed upon power up as shown. (Reject if "blank screen" is displayed)
- ☒ e) Check the date, time as per real time & revision 3.04 is displayed check Error Log default display shown as above (2 cycles only).
- ☒ f) Check all carousels are removed.
- ☒ g) Check solvent condition access door fully contact with magnet latch.
- ☒ h) Check tubing is fully secure into the clips slot.
- ☒ i) Check cable tie is present.
- ☒ j) Check solvent tubings are route inside the clip.
- ☒ k) 3 captive screws are fully tighten.
- ☒ l) 2 head nuts & draw off valve on pump tray are fully tighten. Check 2 head nuts (bottom side) appearance no marred mark.
- ☒ m) Solvent inlet tubing SOLVENT A (yellow), SOLVENT B (blue), SOLVENT C (red) & SOLVENT D (green) are in sequence.

Remarks: *N/A*

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL




SKW-ENG4028-00
Final Inspection Checklist Template


Rev: A
Final Inspection Checklist For
186269506
WAT-RW-SEH00007 Rev AG

Model : 186269506	Checked By : (Employee Number & Sign) 246025 [Signature]	Date : 1 9 - N O V - 2 0 1 8
Serial No. : L18SM4610A	Verified By : (Employee Number & Sign) 836410 [Signature]	Date : 1 9 - N O V - 2 0 1 8


Top view




☒ Wires routed neatly & cables tie are locked (x4).



☒ HPMV screws are fully tighten (x4).





- ☒ a) Ground wire is fully tighten onto chassis.
☒ b) Syringe motor cable is secure with clumper.






☒ Injector & Carousel captive screws are fully tighten (x5).

Left side view



- ☒ a) CPU board is fully secure to chassis with 2 screws.
☒ b) Pump tray cable is fully inserted.
☒ c) Ground wires are fully tighten onto chassis stud (x2).
☒ d) All connectors are fully inserted.
☒ e) Check ' PASSED HI-POT ' stamp is visible, printing no smear & etc.

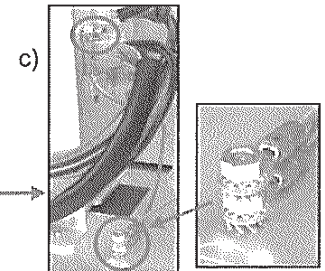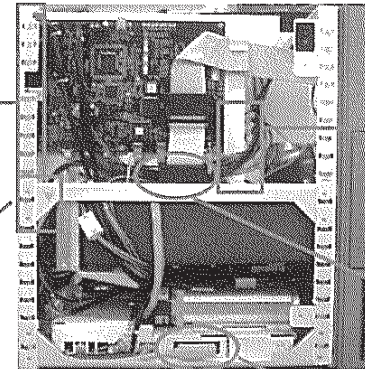

COMPANY CONFIDENTIAL

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Page 2 of 7




SKW-ENG4028-00
Final Inspection Checklist Template

Rev: A
Final Inspection Checklist For
186269506
WAT-RW-SEH00007 Rev AG

Model : 186269506	Checked By : (Employee Number & Sign) 246025 <i>[Signature]</i>	Date : 1 9 - N O V - 2 0 1 8
Serial No. : 2185M4610A	Verified By : (Employee Number & Sign) 836410 <i>[Signature]</i>	Date : 1 9 - N O V - 2 0 1 8

Rear view

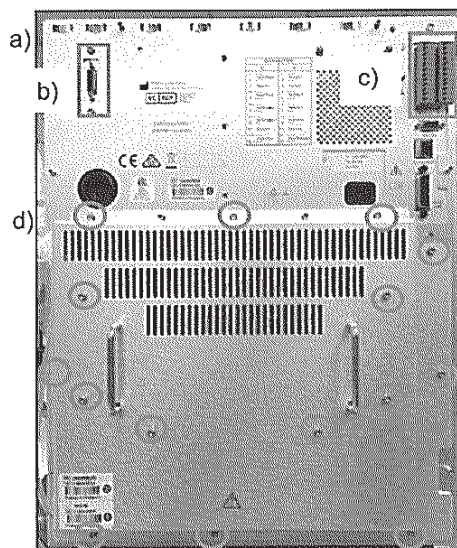

- ☒ a) Overall appearance check, no scratches and stain mark.
- ☒ b) Column heater PCB assembly is fully secure to chassis with 2 screws.
- ☒ c) Confirm I/O A & B connectors are fully inserted.
- ☒ d) 15 screws are fully tighten for heater cooler cover.




Information Set 716003761

Serial no. is visible through envelop opening
Check all items are placed under

- a) Check Certificate in Envelope that matches with instrument S/N and signed
- b) Alliance® e2695 Separations Module System Documentation CD [715003795]
- c) Alliance Interactive System Support DVD [715000116]
- d) Service Solution Sheet

e.g.:



DHR

- a) WATERS CORPORATION 2695 System Pre Check Off Sheet
- b) WATERS CORPORATION – TEST RECORD
- c) Carryover Test, Linearity & Chemistry Tests (AC & BD) result
- d) Waters Corporation SUBASSEMBLY TEST RECORD
- e) WATERS Instrument Assembly Event Log
- f) Final Inspection Checklist for 279003915
- g) Final Inspection Checklist for WAT271290
- h) Final Inspection Checklist For 186269506

COMPANY CONFIDENTIAL

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.

CONFIDENTIAL

28 JAN 2019

**FLEXTRONICS
DOCUMENT CONTROL**


Page 3 of 7

Model : 186269506	Checked By : (Employee Number & Sign) 246025 L	Date : 1 9 - NOV - 2018
Serial No. : L185m4610A	Verified By : (Employee Number & Sign) 836410 LI	Date : 1 9 - NOV - 2018

Labeling location

Verify Instrument label is correct, verify part name, description & serial number are correct.

A) Front view - Syringe door open



a) e.g.:



☒ a) Correct serial no. is pasted on the syringe assembly.

B) Front view - Solvent door open




b) e.g.:




☒ b) Correct caution label is pasted above the solvent door.

C) Top view - Power supply




c) e.g.:




☒ c) Correct warning label is pasted on top of power supply unit.

D) Rear view

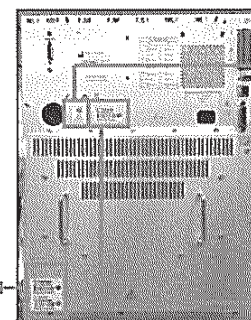

d)

e.g.:



f) e.g.:




e) e.g.:




☒ d) Correct ETL label is pasted.
☒ e) Correct serial no. label is pasted.
☒ f) Correct heater cooler labels are pasted (x2).

E) Startup kit with carousel



e.g.:

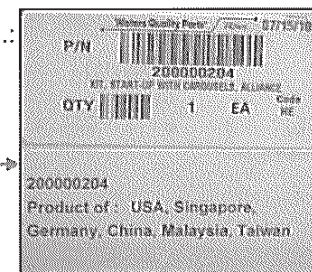

☒ Correct startup kit with carousel used for this model.
☒ Country of origin (COO) should be pasted.



SKW-ENG4028-00

Final Inspection Checklist Template




Rev: A

Final Inspection Checklist For
186269506
WAT-RW-SEH00007 Rev AG

Model : 186269506	Checked By : (Employee Number & Sign) 246025 	Date : 1 9 - N O V - 2 0 1 8
Serial No. : L185M 4610 A	Verified By : (Employee Number & Sign) 836410 	Date : 1 9 - N O V - 2 0 1 8

Overall Check

- ☒ a) No foreign identification tag, arrow stickers, round stickers & etc in the inner and outer of instrument.
- ☒ b) Check overall appearance, no scratches, no stain mark & etc on the instrument.
- ☒ c) Check no missing cable tie, label, screw & etc. All screws must fully tightened.

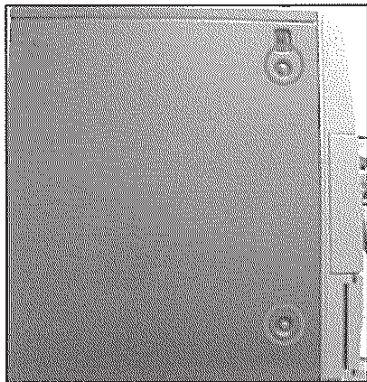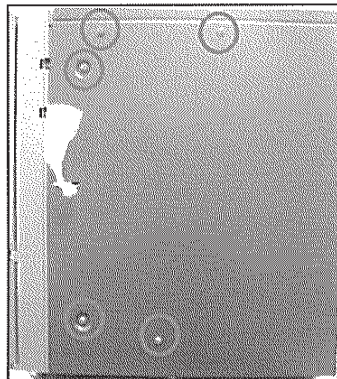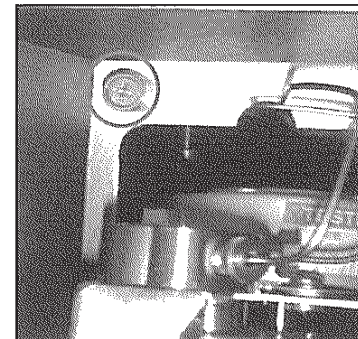a) Left coverb) Right coverc) Syringe door open

- ☒ a) 2 screws are fully tighten for left cover.
- ☒ b) 5 screws are fully tighten for right cover.
- ☒ c) 1 screw is fully tighten for top cover.

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

COMPANY CONFIDENTIAL

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.



SKW-ENG4028-00
Final Inspection Checklist Template

Rev: A
Final Inspection Checklist For
186269506
WAT-RW-SEH00007 Rev AG

Model : 186269506	Checked By : (Employee Number & Sign) 952450 [Signature]	Date : 1 9 - NOV - 2018
Serial No. : L18SM461DA	Verified By : (Employee Number & Sign) 246025 [Signature]	Date : 1 9 - NOV - 2018

Packing location



A) Check no scratches and blemishes when view Front, Top, Right, Left and Rear Panels.


Front Panel




Front Panel




Right Panel

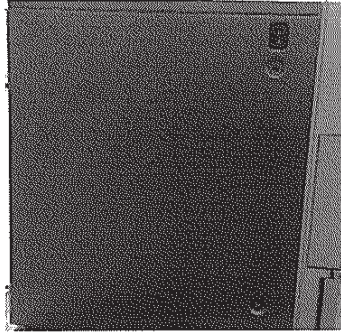


Left Panel

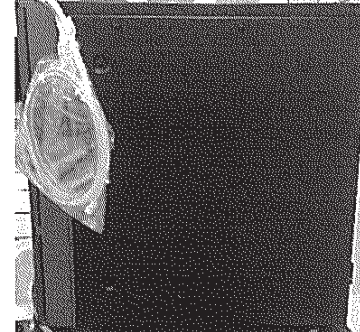

Rear Panel

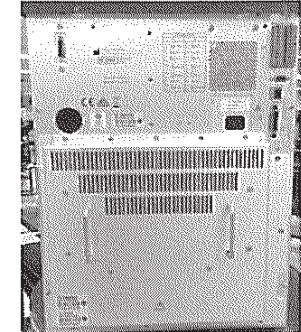

B) Check both side of plastic is loose to prevent Plastic damage

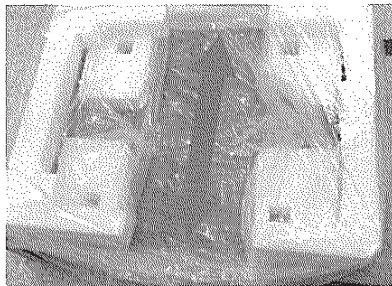

C) After pack check for Plastic not torn & Pallet not damaged.



CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

COMPANY CONFIDENTIAL

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.




SKW-ENG4028-00
Final Inspection Checklist Template


Rev: A
Final Inspection Checklist For
186269506
WAT-RW-SEH00007 Rev AG

Model : 186269506	Checked By : (Employee Number & Sign) 952450 <i>[Signature]</i>	Date : 19 - NOV - 2018
Serial No. : L18SM4610A	Verified By : (Employee Number & Sign) 246025 <i>[Signature]</i>	Date : 19 - NOV - 2018

☒ D) Check Waters
Congratulation label Pasted to
carton box top side as shown.



☒ E) Check placed shipping
label under the perforated
cut out on the box.

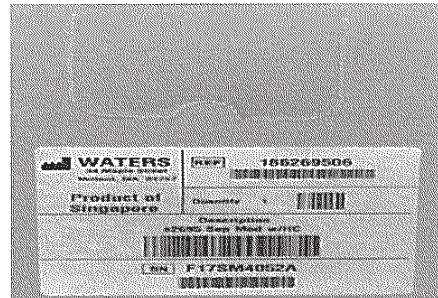

☐ F) Check carton box & pallet in
Good Condition before ship.



☒ G) Paste the long serial number from the preprinted
label in the box provided below :

SN	L18SM4610A	
REF	186269506	

CONFIDENTIAL
28 JAN 2019
FLEXTRONICS
DOCUMENT CONTROL

Model : 186269506


Serial No.: L18SM3610A

Legend [✓]- OK, [X]- NG, [NA]- Not Applicable

Name / Sign / Date: JHURLEY CINA ANAK ADULT R 19 NOV 2018

Front view


a) ~ f)

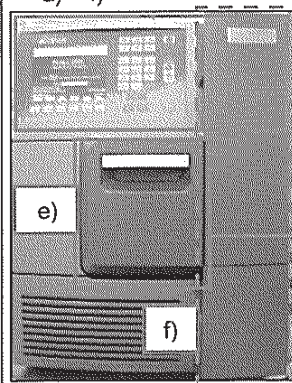


b)

Waters e2695
Separations Module


e)




c)

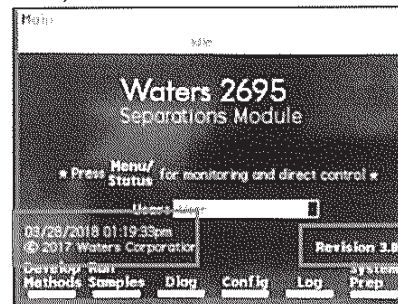


d)

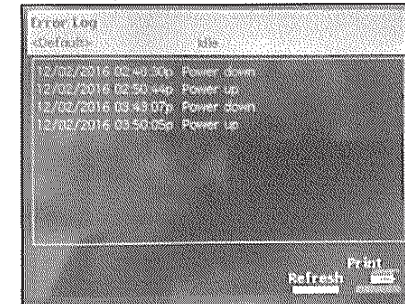**Open the doors**


g) ~ l)

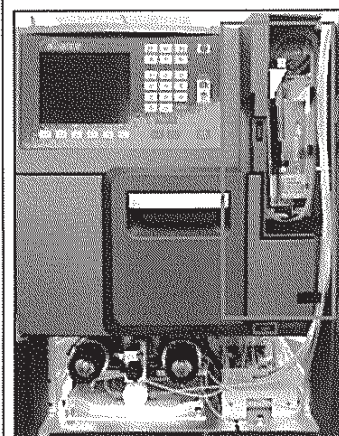


g) ~ i)

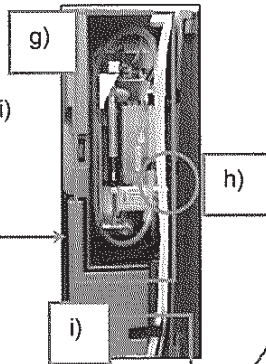

k)



l)



- ☒ a) Overall appearance check, no scratches, no stain mark & etc. Keypad surface also included.
- ☒ b) Check correct label (Waters e2695 Separations Module – all wording is blue color). Protective sheet is removed.
- ☒ c) Check the date, time as per real time. Revision 3.04 is displayed & Check 'Waters' word appears on the screen.
- ☒ d) Check 'Error Log' default display (2 cycles only) before shipment as shown.
- ☒ e) Check all carousels are removed.
- ☒ f) Check syringe door magnet & solvent door magnet are working.
- ☒ g) Check tubing is present & secure into two clips slot.
- ☒ h) Check cable tie is present and cut.
- ☒ i) Check all solvent tubing's are route inside the clip.
- ☒ j) Check 3 captive screws are fully tightened.
- ☒ k) Check 2 head nuts & draw off valve on pump tray are fully tightened. Check 2 head nuts (bottom side) appearance no marred mark.
- ☒ l) Check solvent inlet tubing SOLVENT A (yellow), SOLVENT B (blue), SOLVENT C (red) & SOLVENT D (green) are in sequence as shown.

Remarks : NA

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Model : 186269506

Serial No.:


L18SM46101

Legend: [✓] - OK, [X] - NG, [NA] - Not Applicable


Name / Sign / Date:

OTTERLEY PINA AUK ADUT 9 19 NOV 2018

Top view




Check 4 cables tie are locked.



Check HPMV 4 screws are fully tightened.

a)

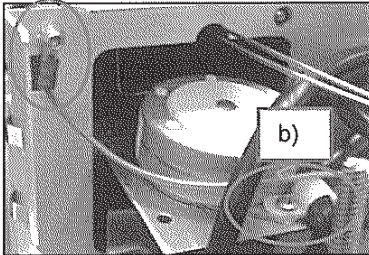



b)



a) Check grounding wire is fully tightened.




b) Check syringe motor cable is secure with clamper.

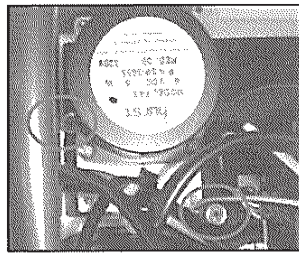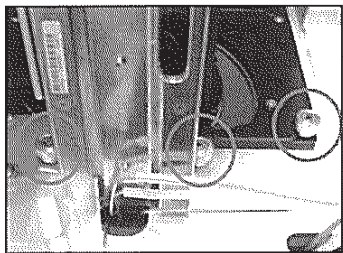

Check injector & carousel 5 captive screws are fully tightened.

Left side view

a)



b)



a) Check CPU board 2 screws are fully tightened.



b) Check ' PASSED HI-POT ' stamp is visible, no printing smear & etc.



c) Check 3 grounding wires are fully tightened.




d) Check CPU to pump drive cable is fully secured.




e) Check all connectors are fully inserted.

c)



d)



d)



CONFIDENTIAL


28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Model : 186269506

Serial No.: L18SM4610A

Legend [✓] - OK, [X] - NG, [NA] - Not Applicable

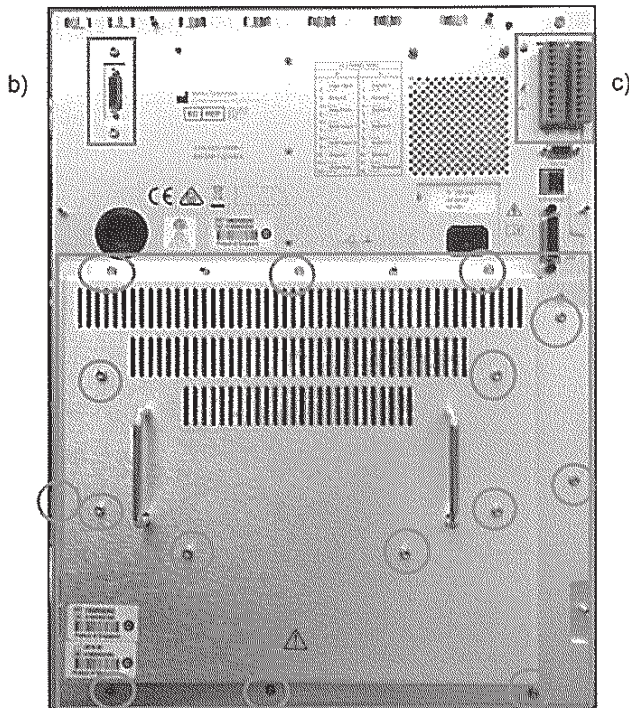Name / Sign / Date: MURLEY TINA ANAK ADUT 9 19 NOV 2018Rear view


- ☒ a) Overall appearance check, no scratches, no stain mark & etc.
- ☒ b) Check column heater PCB assembly 2 screws are fully tightened.
- ☒ c) Check I/O A & B connectors are present & fully inserted.
- ☒ d) Check heater cooler assembly 15 screws are fully tightened.

☒ **Information Set 716003761**

Check serial no. is visible through envelope opening & all items are placed as below:

- a) Certificate Of Functional Performance
- b) Alliance® e2695 Separations Module System Documentation [CD-ROM] [715003795]
- c) Alliance Interactive System Support DVD for e2695 Separations Module [715000116]
- d) Service Solution Sheet

e.g.:

**CONFIDENTIAL**

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL**COMPANY CONFIDENTIAL**

This Document is controlled in QDMS. All Copies (electronic or printed) are considered uncontrolled.

Model : 186269506

Serial No.: L18SM46104

Legend: [✓] - OK, [X] - NG, [NA] - Not Applicable

Name / Sign / Date: ✓ HURLEY TINA INAC ADUT 9 19 NOV 2018

Labeling location

Verify Instrument label is correct; verify part name, description & serial number are correct.

A) Front view - Syringe door open




a) e.g.:




☒ a) Check correct serial no. is pasted on the syringe assembly.

C) Top view - Power supply




c) e.g.:




☒ c) Check correct warning label (top of power supply) is pasted.

B) Front view - Solvent door open



b) e.g.:



☒ b) Check correct caution label is pasted.

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL

Model : 186269506

Serial No.:

L18SM46109

Legend [✓] - OK, [X] - NG, [NA] - Not Applicable


Name / Sign / Date:

JACLEY TINA ANAC ADUT 2

19 NOV 2018

Labeling location


Verify Instrument label is correct; verify part name, description & serial number are correct.

D) Rear view

f) e.g.:




d) e.g.:




e) e.g.:



- ☒ d) Check correct ETL label is pasted.
- ☒ e) Check correct serial no. label is pasted.
- ☒ f) Check correct heater cooler 2 labels are pasted.

E) Startup kit with carousel

e.g.:

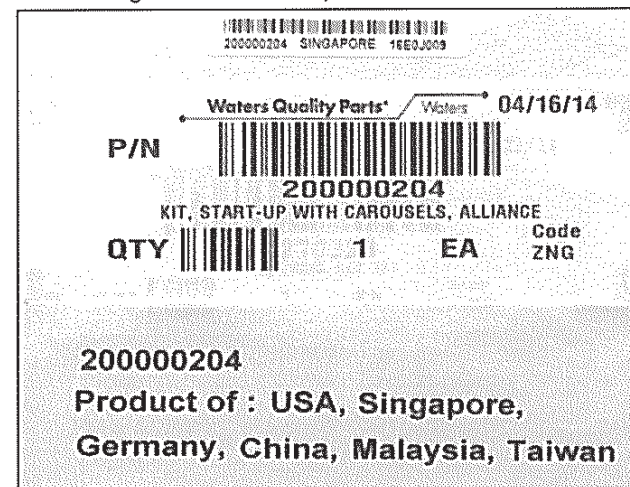

- ☒ Check correct startup kit with carousels (200000204) & country of origin (COO) is pasted.

CONFIDENTIAL

28 JAN 2019



FLEXTRONICS
DOCUMENT CONTROL

Model : 186269506

Serial No.: L185014610A

Legend: [✓] - OK, [X] - NG, [NA] - Not Applicable

Name / Sign / Date: MURLEY EVA MAK 2017 9 19 NOV 2018

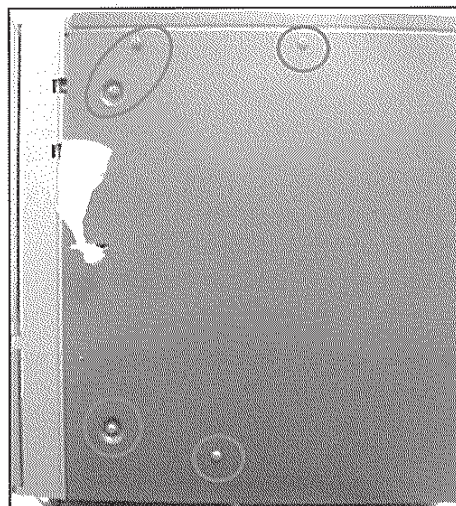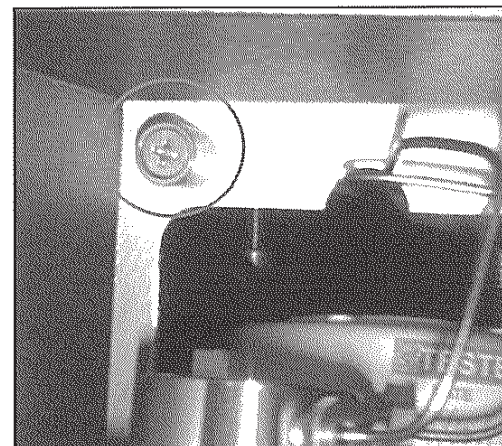All cover with screws as below :a) Left side coverb) Right coverc) Syringe door open

- ☒ a) Check left cover 2 screws are fully tightened.
- ☒ b) Check right cover 5 screws are fully tightened.
- ☒ c) Check top cover screw is fully tightened.

Overall Check

- ☒ a) No foreign identification tag, arrow stickers, round stickers & etc. in the inner and outer of instrument.
- ☒ b) Check overall appearance, no scratches, no stain mark & etc. on the instrument.
- ☒ c) Check no missing cable tie, label, screw & etc. All screws must fully tightened.

☒ DHR

- a) WATERS CORPORATION 2695 System Pre Check Off Sheet
- b) WATERS CORPORATION – TEST RECORD
- c) Carryover Test, Linearity Test & Chemistry Tests (AC & BD) result
- d) Waters Corporation SUBASSEMBLY TEST RECORD
- e) WATERS Instrument Assembly Event Log
- f) Final Inspection Checklist For 279003915
- g) Final Inspection Checklist For WAT271290
- h) Final Inspection Checklist For 186269506
- i) FQA Inspection Checklist For 186269506

CONFIDENTIAL

28 JAN 2019

FLEXTRONICS
DOCUMENT CONTROL
