



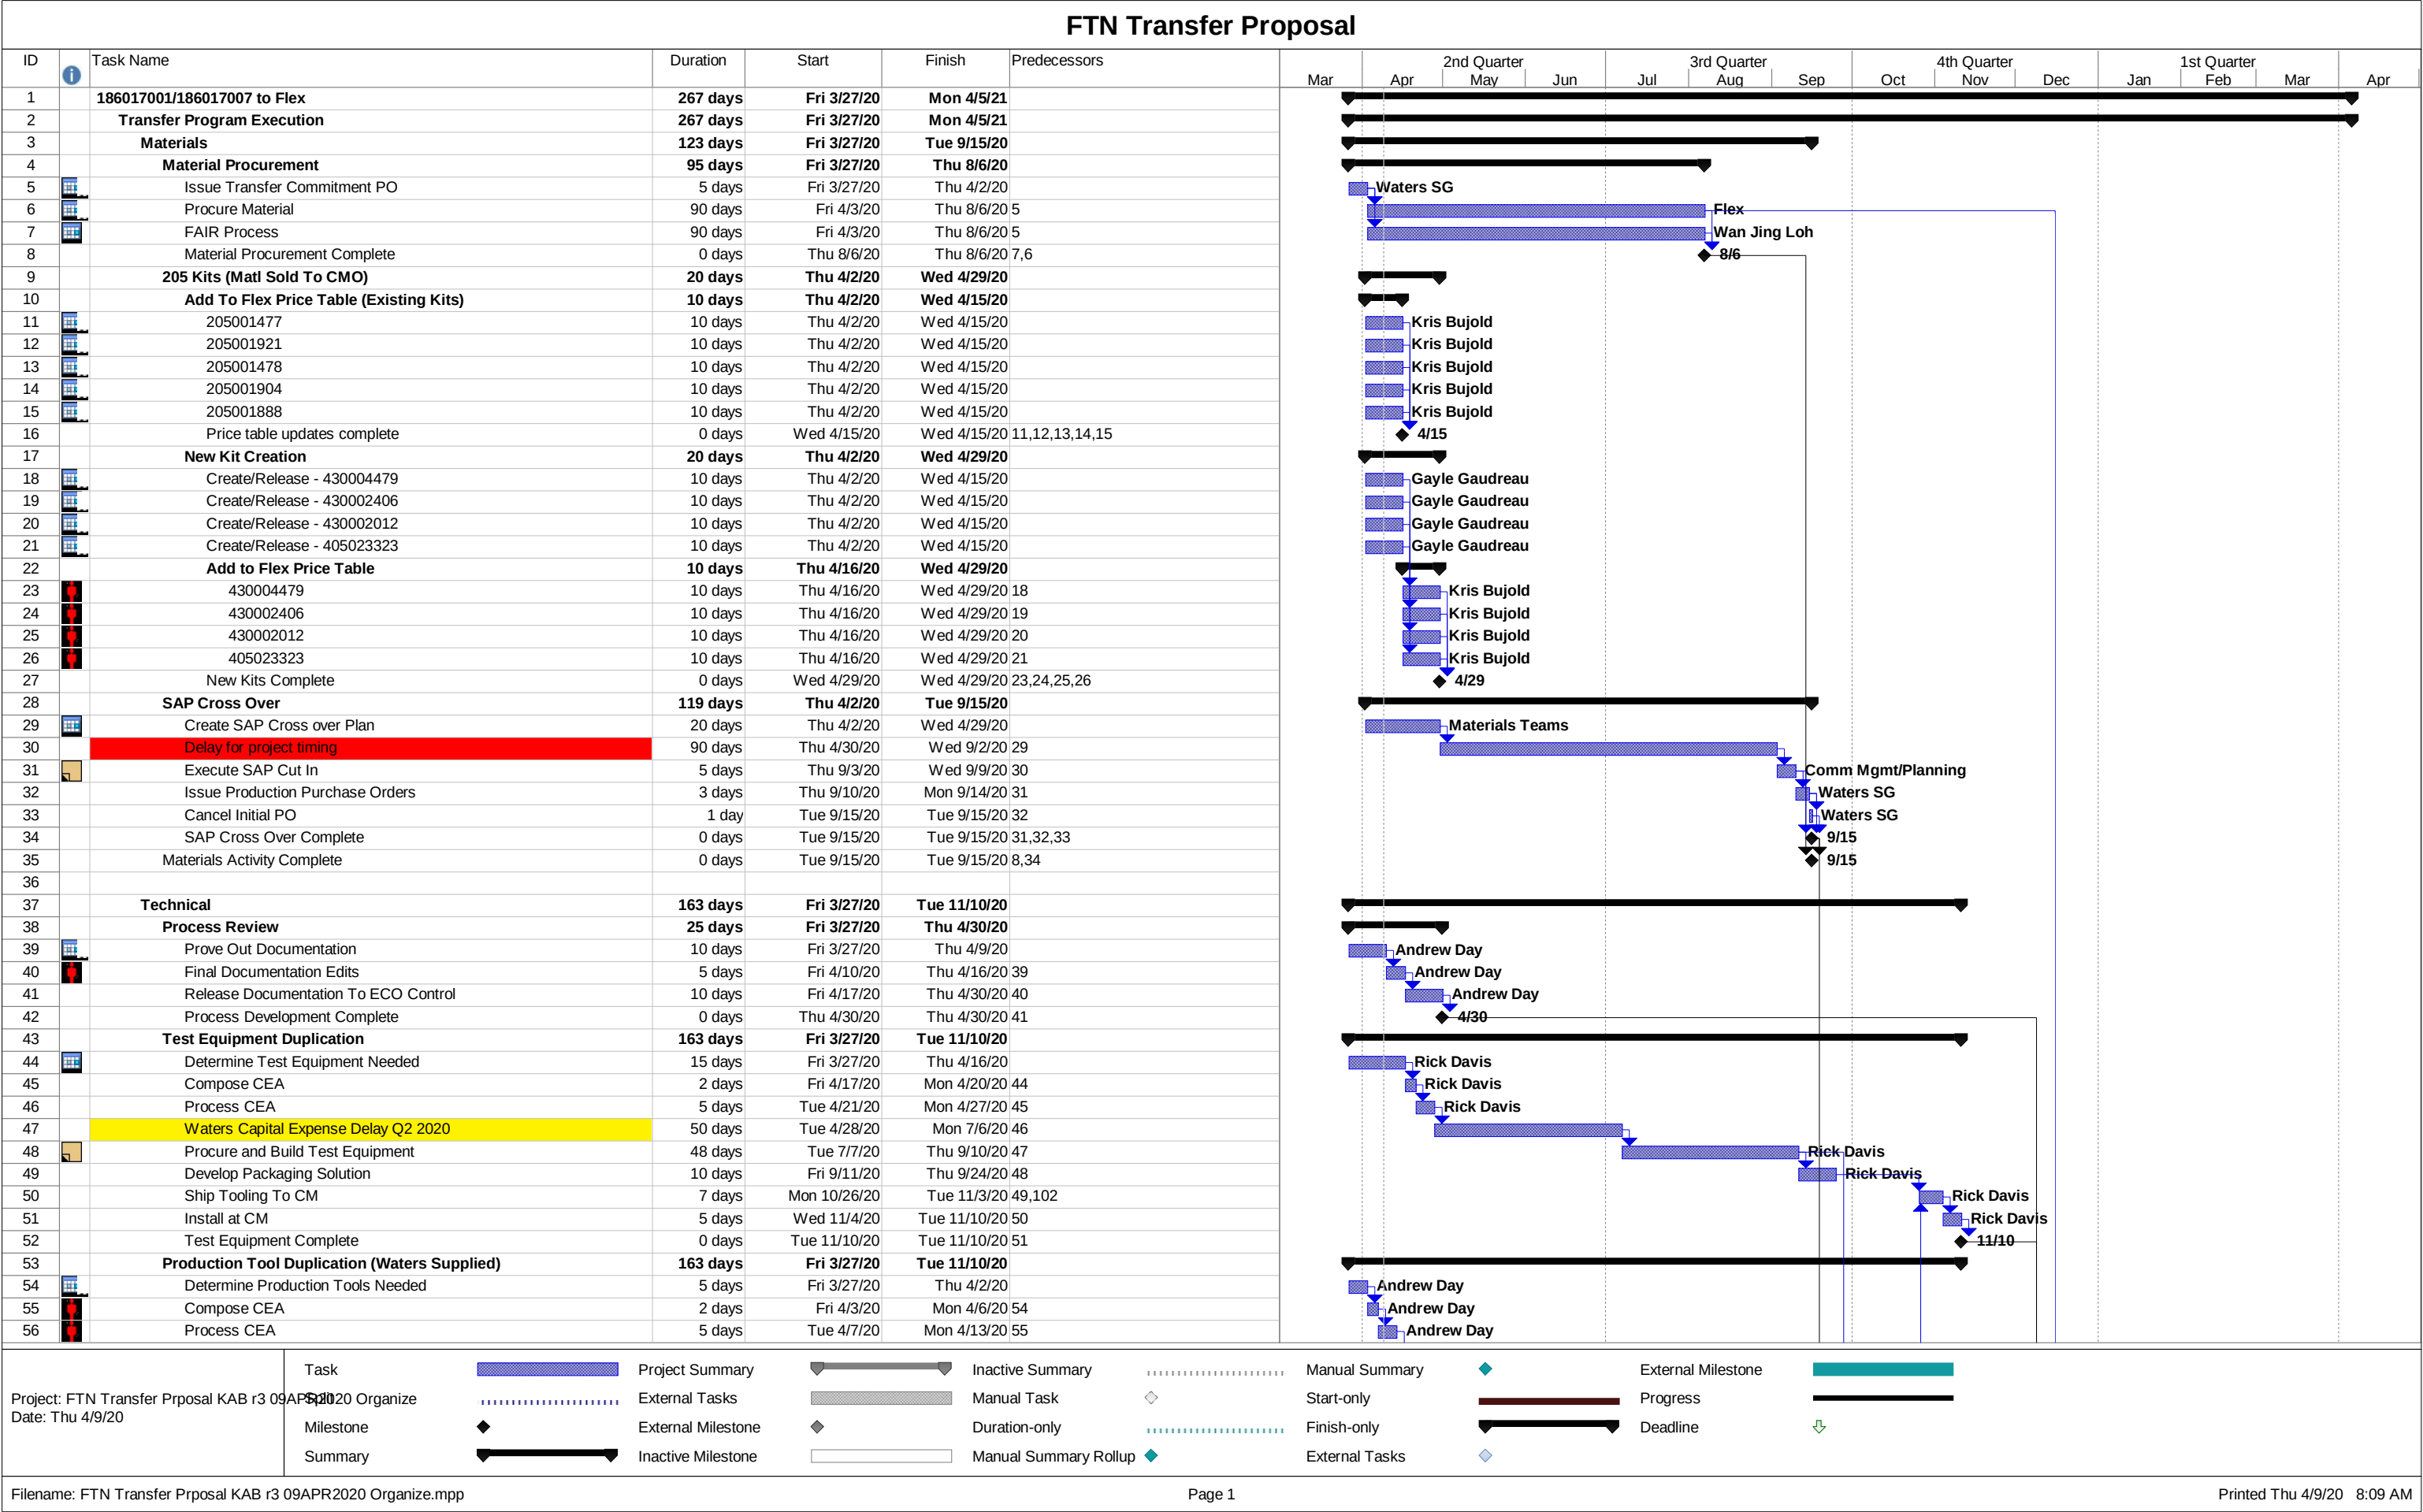

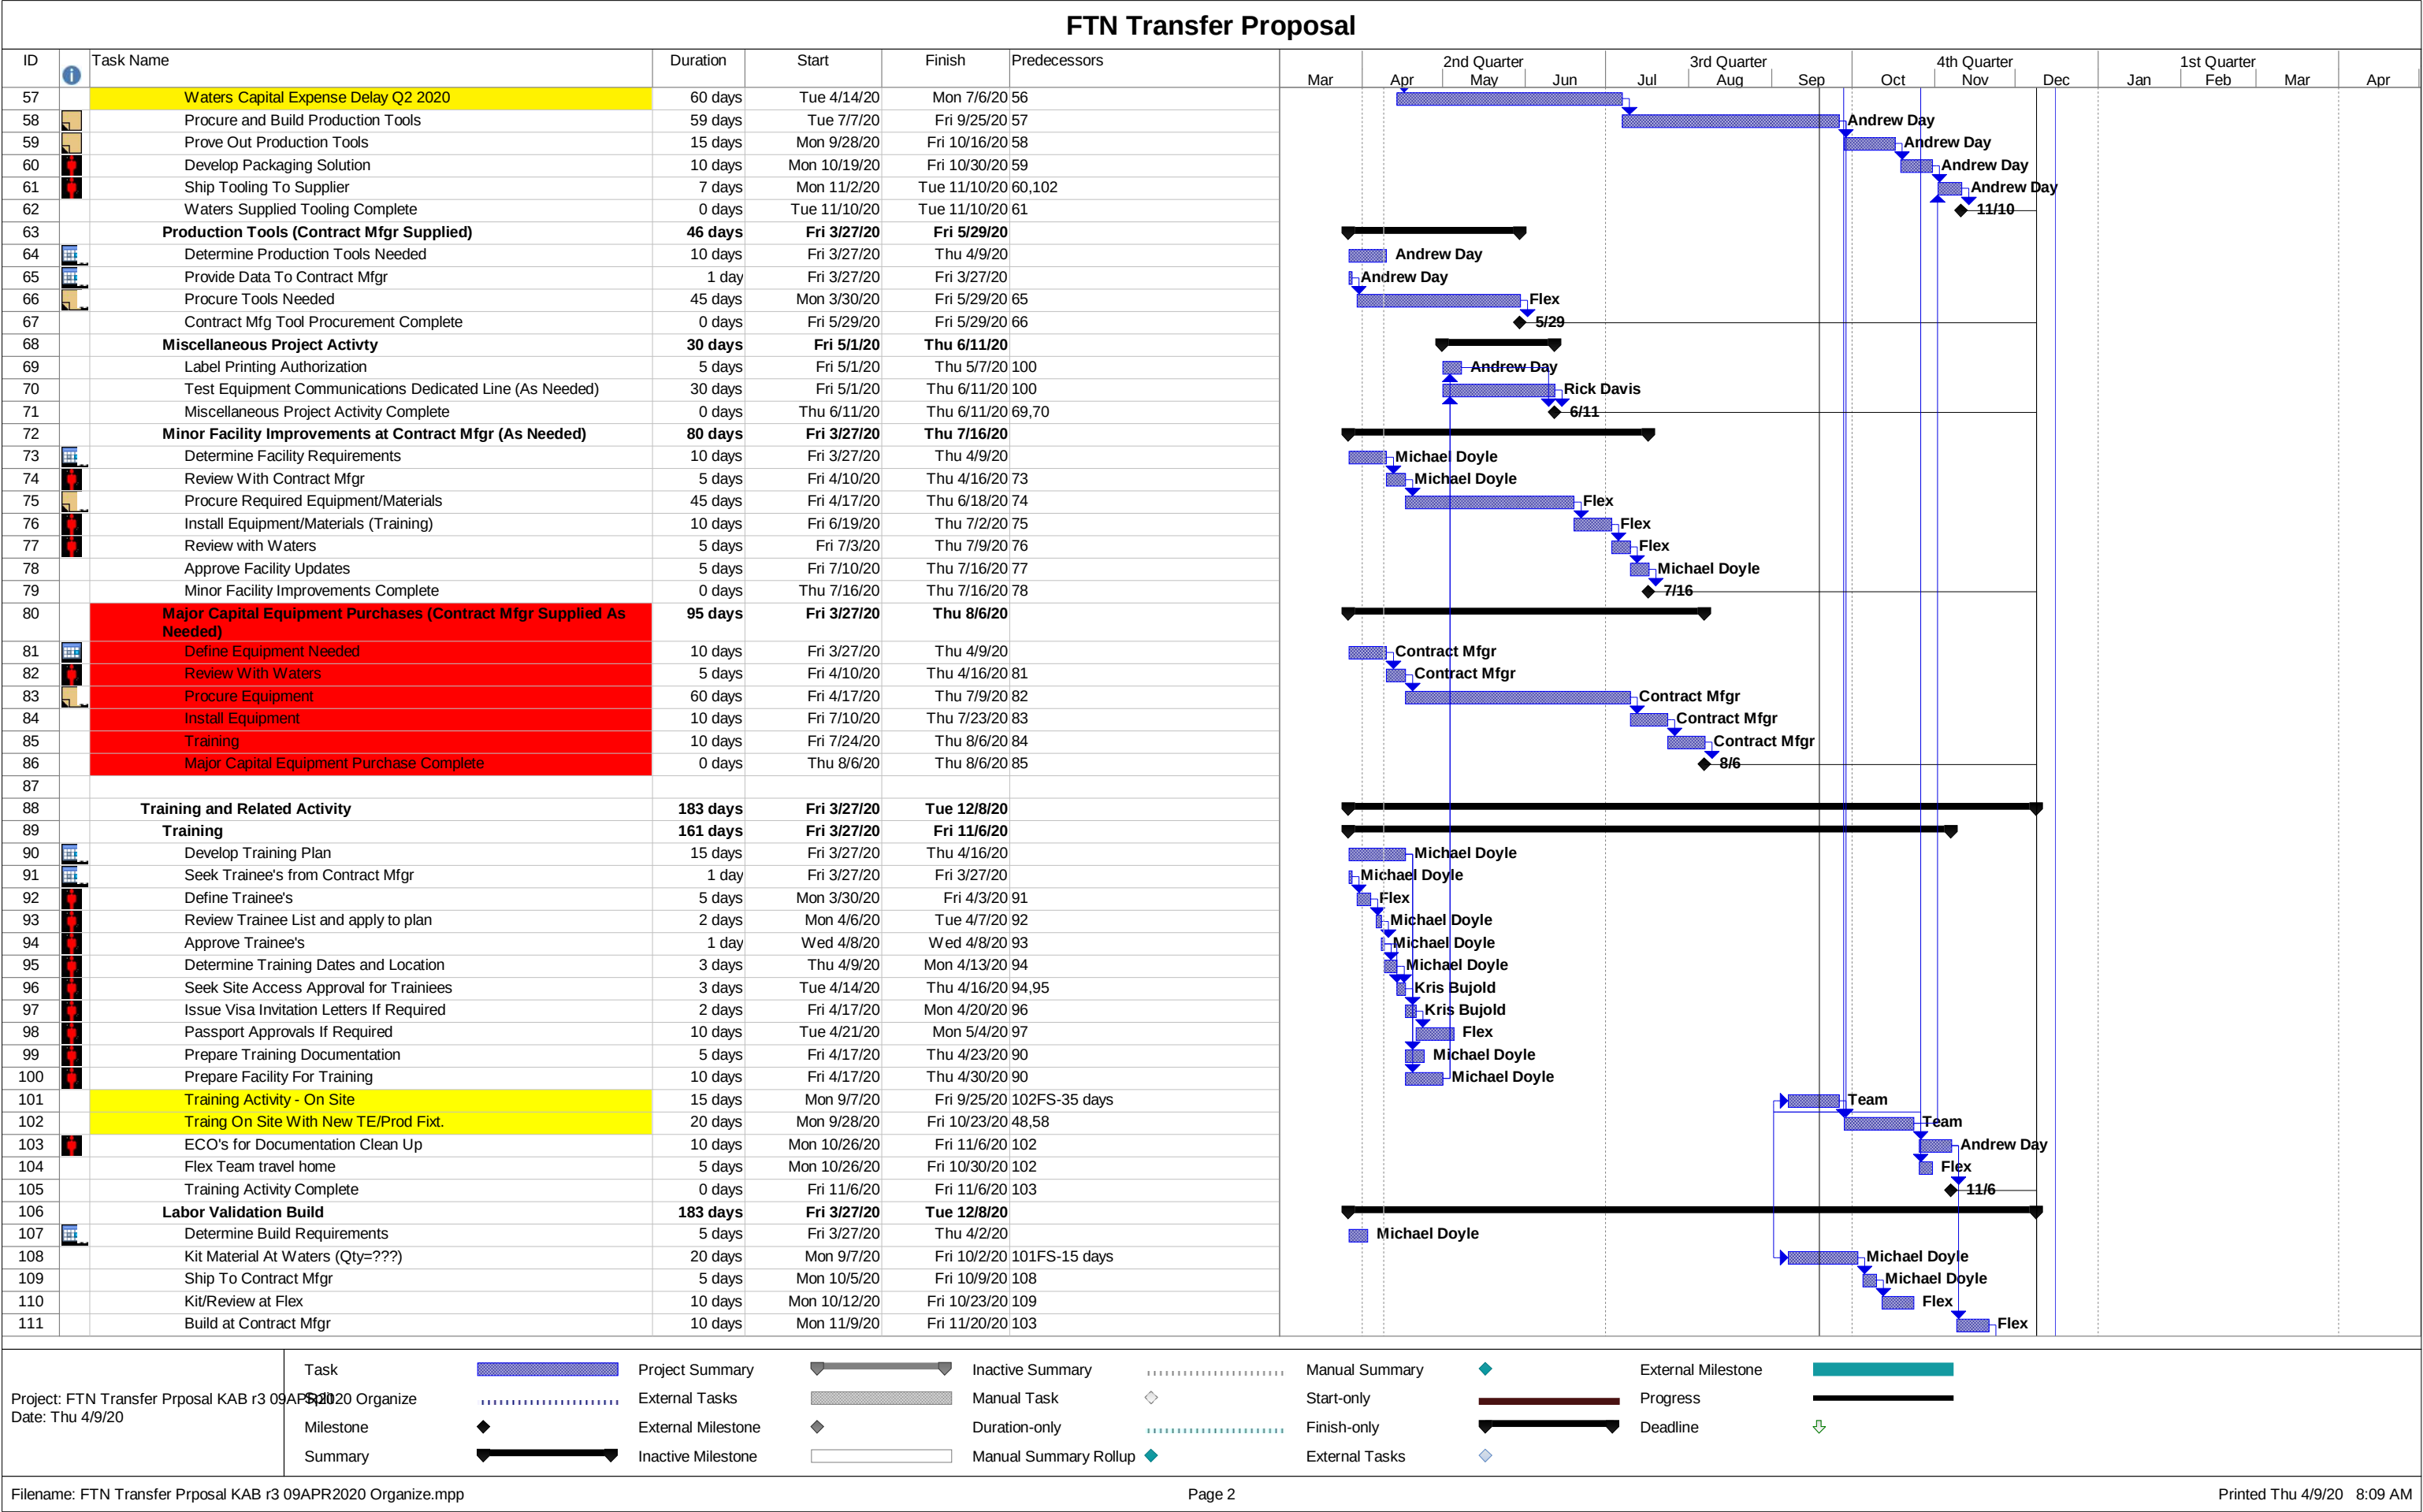

FTN Transfer Proposal

ID	Task Name	Duration	Start	Finish	Predecessors	Mar	Apr	2nd Quarter	May	Jun	Jul	3rd Quarter	Aug	Sep	Oct	4th Quarter	Nov	Dec	Jan	1st Quarter	Feb	Mar	Apr
112	Ship To Waters For Review	7 days	Mon 11/23/20	Tue 12/1/20	111																		
113	Review At Waters / Issue Report	5 days	Wed 12/2/20	Tue 12/8/20	112																		
114	Validation Build Complete	0 days	Tue 12/8/20	Tue 12/8/20	113																		
115																							
116	Production Builds	267 days	Fri 3/27/20	Mon 4/5/21																			
117	Pre-Production Build / Mfg Qual Readiness	207 days	Fri 3/27/20	Mon 1/11/21																			
118	Establish Build Plan	20 days	Wed 9/16/20	Tue 10/13/20	34																		
119	Provide Purchase Orders	5 days	Wed 10/14/20	Tue 10/20/20	118																		
120	Compose Mfg Qual Readiness Plan	15 days	Fri 3/27/20	Thu 4/16/20																			
121	Review for program readiness	5 days	Wed 12/9/20	Tue 12/15/20	42,52,62,105,114,67,79,86,71,120																		
122	Kit Material At Contract Mfgr	5 days	Wed 12/16/20	Tue 12/22/20	6,121																		
123	EQQ / Holiday Delay	13 days	Wed 12/16/20	Fri 1/1/21	121																		
124	Mfg Qual Readiness Build	5 days	Mon 1/4/21	Fri 1/8/21	123																		
125	Sustaining Production Starts	1 day	Mon 1/11/21	Mon 1/11/21	124																		
126	Qual Readiness Complete	0 days	Mon 1/11/21	Mon 1/11/21	125																		
127	Qual Readiness Documentation	30 days	Mon 1/11/21	Fri 2/19/21																			
128	Provide Data to Milford for report	5 days	Mon 1/11/21	Fri 1/15/21	124																		
129	Mfg Qual Readiness Report	30 days	Mon 1/11/21	Fri 2/19/21	124																		
130	Mfg Qual Readiness Complete	0 days	Fri 2/19/21	Fri 2/19/21	129																		
131	Dual Builds Flex/Milford	60 days	Mon 1/11/21	Fri 4/2/21																			
132	Dual Builds Milford	60 days	Mon 1/11/21	Fri 4/2/21	124																		
133	Dual Builds Flex	60 days	Mon 1/11/21	Fri 4/2/21	124																		
134	Dual Builds Complete	0 days	Fri 4/2/21	Fri 4/2/21	132,133																		
135	Full Production - Flex	1 day	Mon 4/5/21	Mon 4/5/21																			
136	Full Production - Flex	1 day	Mon 4/5/21	Mon 4/5/21	134																		
137	Full Procustion Complete	0 days	Mon 4/5/21	Mon 4/5/21	136																		
138																							
139	Related Program Activity	306 days	Fri 3/27/20	Fri 5/28/21																			
140	Spares Activity	275 days	Fri 3/27/20	Thu 4/15/21																			
141	Define Spares To Be Transferred	10 days	Fri 3/27/20	Thu 4/9/20																			
142	Prepare/Send RFQ Packages	10 days	Fri 3/27/20	Thu 4/9/20																			
143	Quote Assemblies	30 days	Fri 4/10/20	Thu 5/21/20	142																		
144	Review Quotes / Resolve Issues	10 days	Fri 5/22/20	Thu 6/4/20	143																		
145	Award Quote To Contract Mfgr / Change SAP Demands	3 days	Tue 1/12/21	Thu 1/14/21	125																		
146	Procure Material	60 days	Fri 1/15/21	Thu 4/8/21	145																		
147	Build Spares	5 days	Fri 4/9/21	Thu 4/15/21	146																		
148	Initial Spares Activity Complete	0 days	Thu 4/15/21	Thu 4/15/21	147																		
149	ETL Compliance Certification At Contract Mfgr	100 days	Mon 1/11/21	Fri 5/28/21																			
150	Internal Activity	60 days	Mon 1/11/21	Fri 4/2/21																			
151	Add CM to report	60 days	Mon 1/11/21	Fri 4/2/21	124																		
152	External Activity	40 days	Mon 4/5/21	Fri 5/28/21																			
153	Set Up Facility Audit	20 days	Mon 4/5/21	Fri 4/30/21	151																		
154	Perform Facility Audit	5 days	Mon 5/3/21	Fri 5/7/21	153																		
155	Complete Audit Forms	5 days	Mon 5/10/21	Fri 5/14/21	154																		
156	Audit Reports	10 days	Mon 5/17/21	Fri 5/28/21	155																		
157	ETL Activity Complete	0 days	Fri 5/28/21	Fri 5/28/21	151,156																		
158	Dock To Stock	272 days	Fri 3/27/20	Mon 4/12/21																			
159	Compose Plan	30 days	Fri 3/27/20	Thu 5/7/20																			
160	Dock To Stock Review Period	60 days	Mon 1/11/21	Fri 4/2/21	124																		
161	Dock To Stock Data Review	5 days	Mon 4/5/21	Fri 4/9/21	160																		
162	Dock To Stock Decision	1 day	Mon 4/12/21	Mon 4/12/21	161																		
163	Dock To Stock Complete	0 days	Mon 4/12/21	Mon 4/12/21	162																		

Project: FTN Transfer Proposal KAB r3 09APR20 Date: Thu 4/9/20	Task		Project Summary		Inactive Summary		Manual Summary		External Milestone	
	Summary		External Tasks		Manual Task		Start-only		Progress	
	Milestone		External Milestone		Duration-only		Finish-only		Deadline	
	Summary		Inactive Milestone		Manual Summary Rollup		External Tasks			
